

Cp Long/Eagle

7 Feb 06 (4th Response)

CP LONG/EAGLE SNOW FALL HISTORY 05-06		
DATE	TIME	SNOW
07 Feb 06	0200 - 1300	2-inches
21 Dec	0900 -	.5-inches

CP Eagle/Long			
Beginning of season	Used Year to Date	Currently O/H	
Urea O/H	41,500 lbs.	5,375 lbs.	36,125 lbs.
Calcium O/H	63,500 lbs.	9,750 lbs.	53,750 lbs.

- From 0745 to 1530 7 FEB - Cp Long/Eagle, crews conducted snow removal operations of the Airfield and Priority 1 roads.
- Two Graders, one each Scoop Loader, Snow Blower/sweeper/plow, (1) urea Spreader Truck, and two TMP Bongos conducted snow removal operations.
- 8,000 lbs. of Calcium Chloride & 3,250 lbs. Urea were expended for this mission.
- Trucks have been re-loaded, crews prepared for next response.

Cp Humphrey's

07 Feb 06 (11th Response)

CP HUMPHREY'S SNOW FALL HISTORY 05-06

DATE	TIME	SNOW
07 Jan 06	0135 - 1545	5.2-inches
06 Jan 06	0530 - 0800	Trace
01 Jan 06	1830 - 2100	Trace
25 Dec 05	0835 - 1000	Trace
22 Dec 05	1620 - 1900	.5-inches
21 Dec 05	0530 - 0815	1.7-inches
18 Dec 05	1100 - 1500	2-inches
14 Dec 05	1830 - 2400	1.7-inches

CP Humphrey's			
Beginning of Season Inventory	Received Year to Date	Used Year to Date	Currently O/H
Urea O/H 67,500 lbs.		67,700 lbs.	32,300 lbs.
22 Dec 05 re-supply	15,000		
23 Dec 05 re-supply	17,500		
Calcium O/H 78,300 lbs		20,700 lbs	57,600 lbs.

Weather Reports Received for this Response

Forecast:

- Q Snow \geq 2-inches in 12 Hours.
2-inches is forecast.

Received
0112-hrs
07 Jan 06



Received
0313-hrs
07 Jan 06



Received
0953-hrs
07 Jan 06



Forecast:

- Q Snow \geq 2-inches in 12 Hours.
2-inches is forecast.

Forecast:

- Q Snow \geq 2-inches in 12 Hours.
4-inches is forecast.

Between 0135-1545-hrs 5.2 inches of snow accumulated on Cp Humphrey's.

7 Feb 06

Anjung-Ri



- Photo taken 0545 7 Feb 06. This is main street leading to Cp Humphrey's.

Cp Humphrey's Memorial Park



- **From 0330 to 1630 7 FEB - Cp Humphreys, B&G crews conducted snow removal operations of the Airfield, priority 1, 2, & 3 roads.**
- **Self Help store opened 0635, issued 23 snow shovels, 6 snow blowers, & 400 lbs. of calcium.**

Desiderio Airfield (A-511)



- **Two Graders, (1) Airfield Sweeper, (1) Urea Spreader Trucks, conducted snow removal operations on the airfield.**
- **A hydraulic hose burst on the grader causing a one-hour operational delay while mechanics fabricated and replaced part.**

Freedom Road



- 1,000 lbs. of Calcium Chloride was used on Cp Humphreys road network.

Desiderio Airfield (A-511)



- **Hydraulics on the snow plow failed - mechanics repaired problem.**
- **Eight expendable grader blades were replaced at a cost of \$35. each.**
- **No Urea was expended on the Airfield.**



Take the Time and Spend a Little Time Under The Oak

To Ensure that Your Personnel Are Ready to Work Outside In The Winter Environment.


Make Sure ALL Previous Cold Weather Injuries have been Identified, Your people are counting on YOU.

Area III HQ's



7 Feb 06

Down Town Area

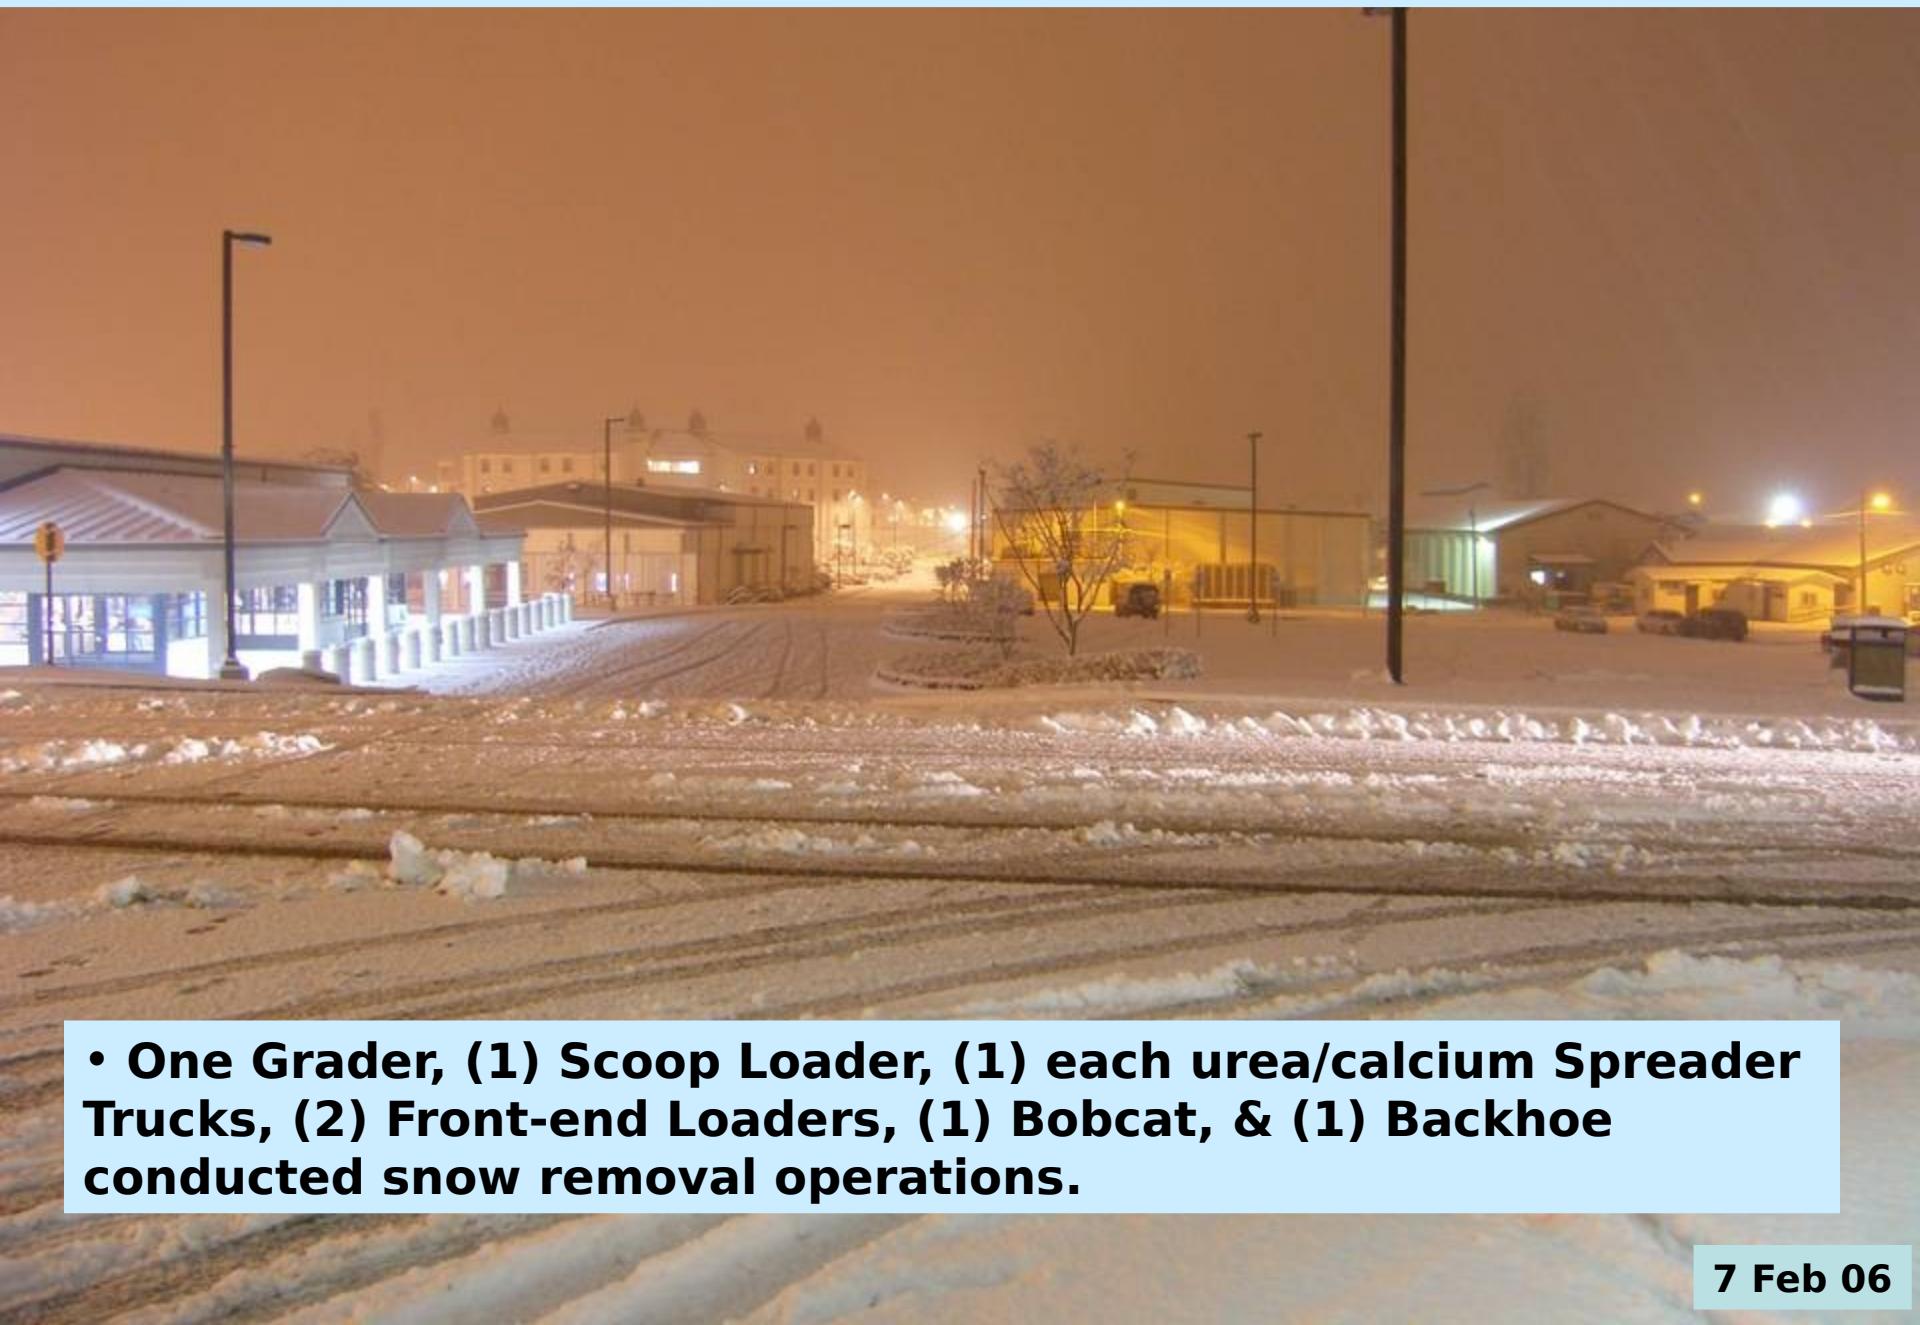

- One Grader, (1) Scoop Loader, (1) each urea/calcium Spreader Trucks, (2) Front-end Loaders, (1) Bobcat, & (1) Backhoe conducted snow removal operations.

HQ USASA Parking Area



7 Feb 06

SNOW VAN



7 Feb 06

Transformation Park



- **Anticipate more snow for this evening or early morning.**
- **Trucks have been re-loaded, B&G crews prepared for next response.**
